

Tuscany by the Sea Car 1

Project Schedule


SIMPLE GANTT CHART by Vertex42.com
<https://www.vertex42.com/ExcelTemplates/simple-gantt-chart.html>

TASK	ASSIGNED TO	PROGRESS	START	END
Contract				
Product Submittals			6/16//25	7/31/25
Product submittal review			6/16/25	7/31/25
Submittal approval			6/16/25	5/30/25
Equipment lead time			6/30/25	11/7/25
Installation			10/6/25	2/6/25
Substantial completion			2/10/25	2/10/25
Final completion			2/14/25	2/14/25
Modernization Start				
Mobilization			10/6/25	10/7/25
Tear out old controller and motor			10/6/25	10/10/25
Install new controller and motor and related equip.			10/13/25	10/17/25
Wire up machine and controller			10/20/25	10/24/25
Cable up machine and car			10/27/25	10/31/25
Install fixtures			11/3/25	11/7/25
Install door operator and light ray			11/10/25	11/14/25
Complete wiring			11/17/25	11/21/25

Project start: Mon, 10/6/2025

Display week: 1

Oct 6, 2025							Oct 13, 2025							Oct 20, 2025							Oct 27, 2025							Nov		
6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W

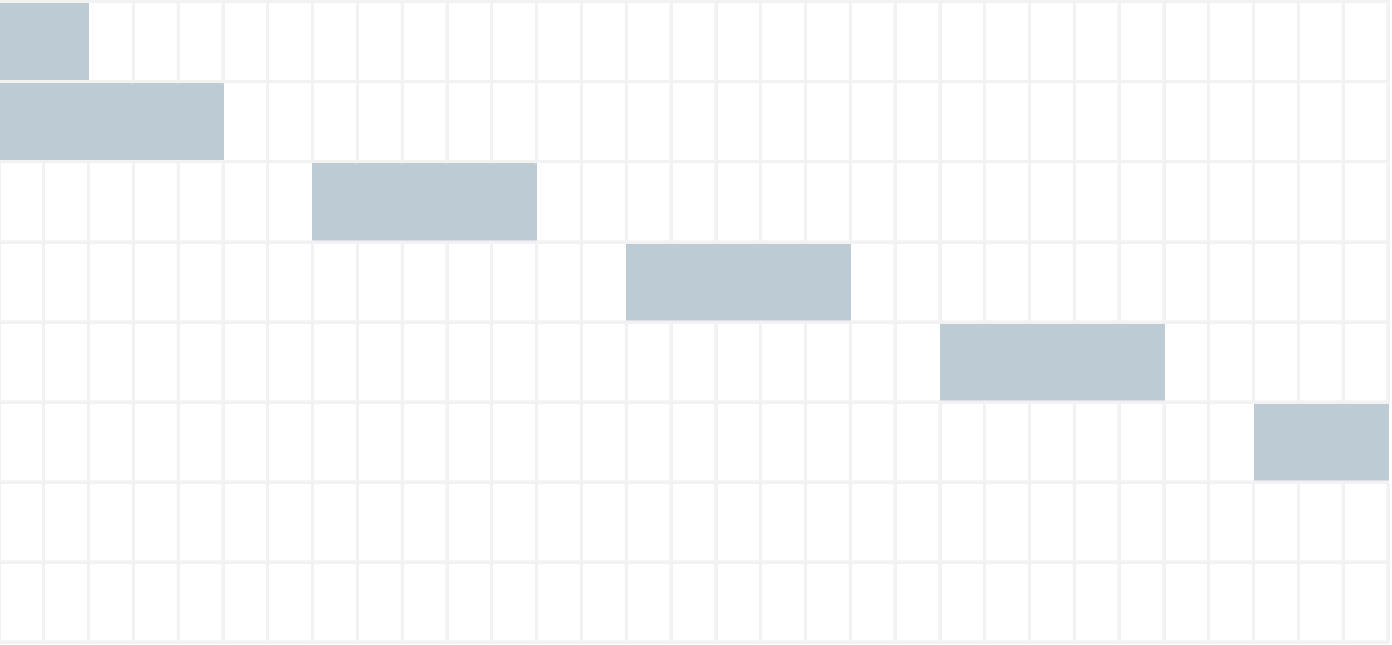

TASK	ASSIGNED TO	PROGRESS	START	END
Adjust elevator			11/24/25	11/26/25
Inspection			12/1/25	12/1/25

1/0/00

Insert new rows ABOVE this one

[illegible]

3, 2025				Nov 10, 2025				Nov 17, 2025				Nov 24, 2025				Dec 1, 2025							Dec 8, 2025															
6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Dec 15, 2025							Dec 22, 2025							Dec 29, 2025						
15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Jan 5, 2026						
5	6	7	8	9	10	11
M	T	W	T	F	S	S

Jan 5, 2026						
5	6	7	8	9	10	11
M	T	W	T	F	S	S
